


WESTERN RAILWAY(CONSTRUCTION)
MAP SHOWING THE ONGOING PROJECTS UNDER WR
(AS ON 11.05.2026)

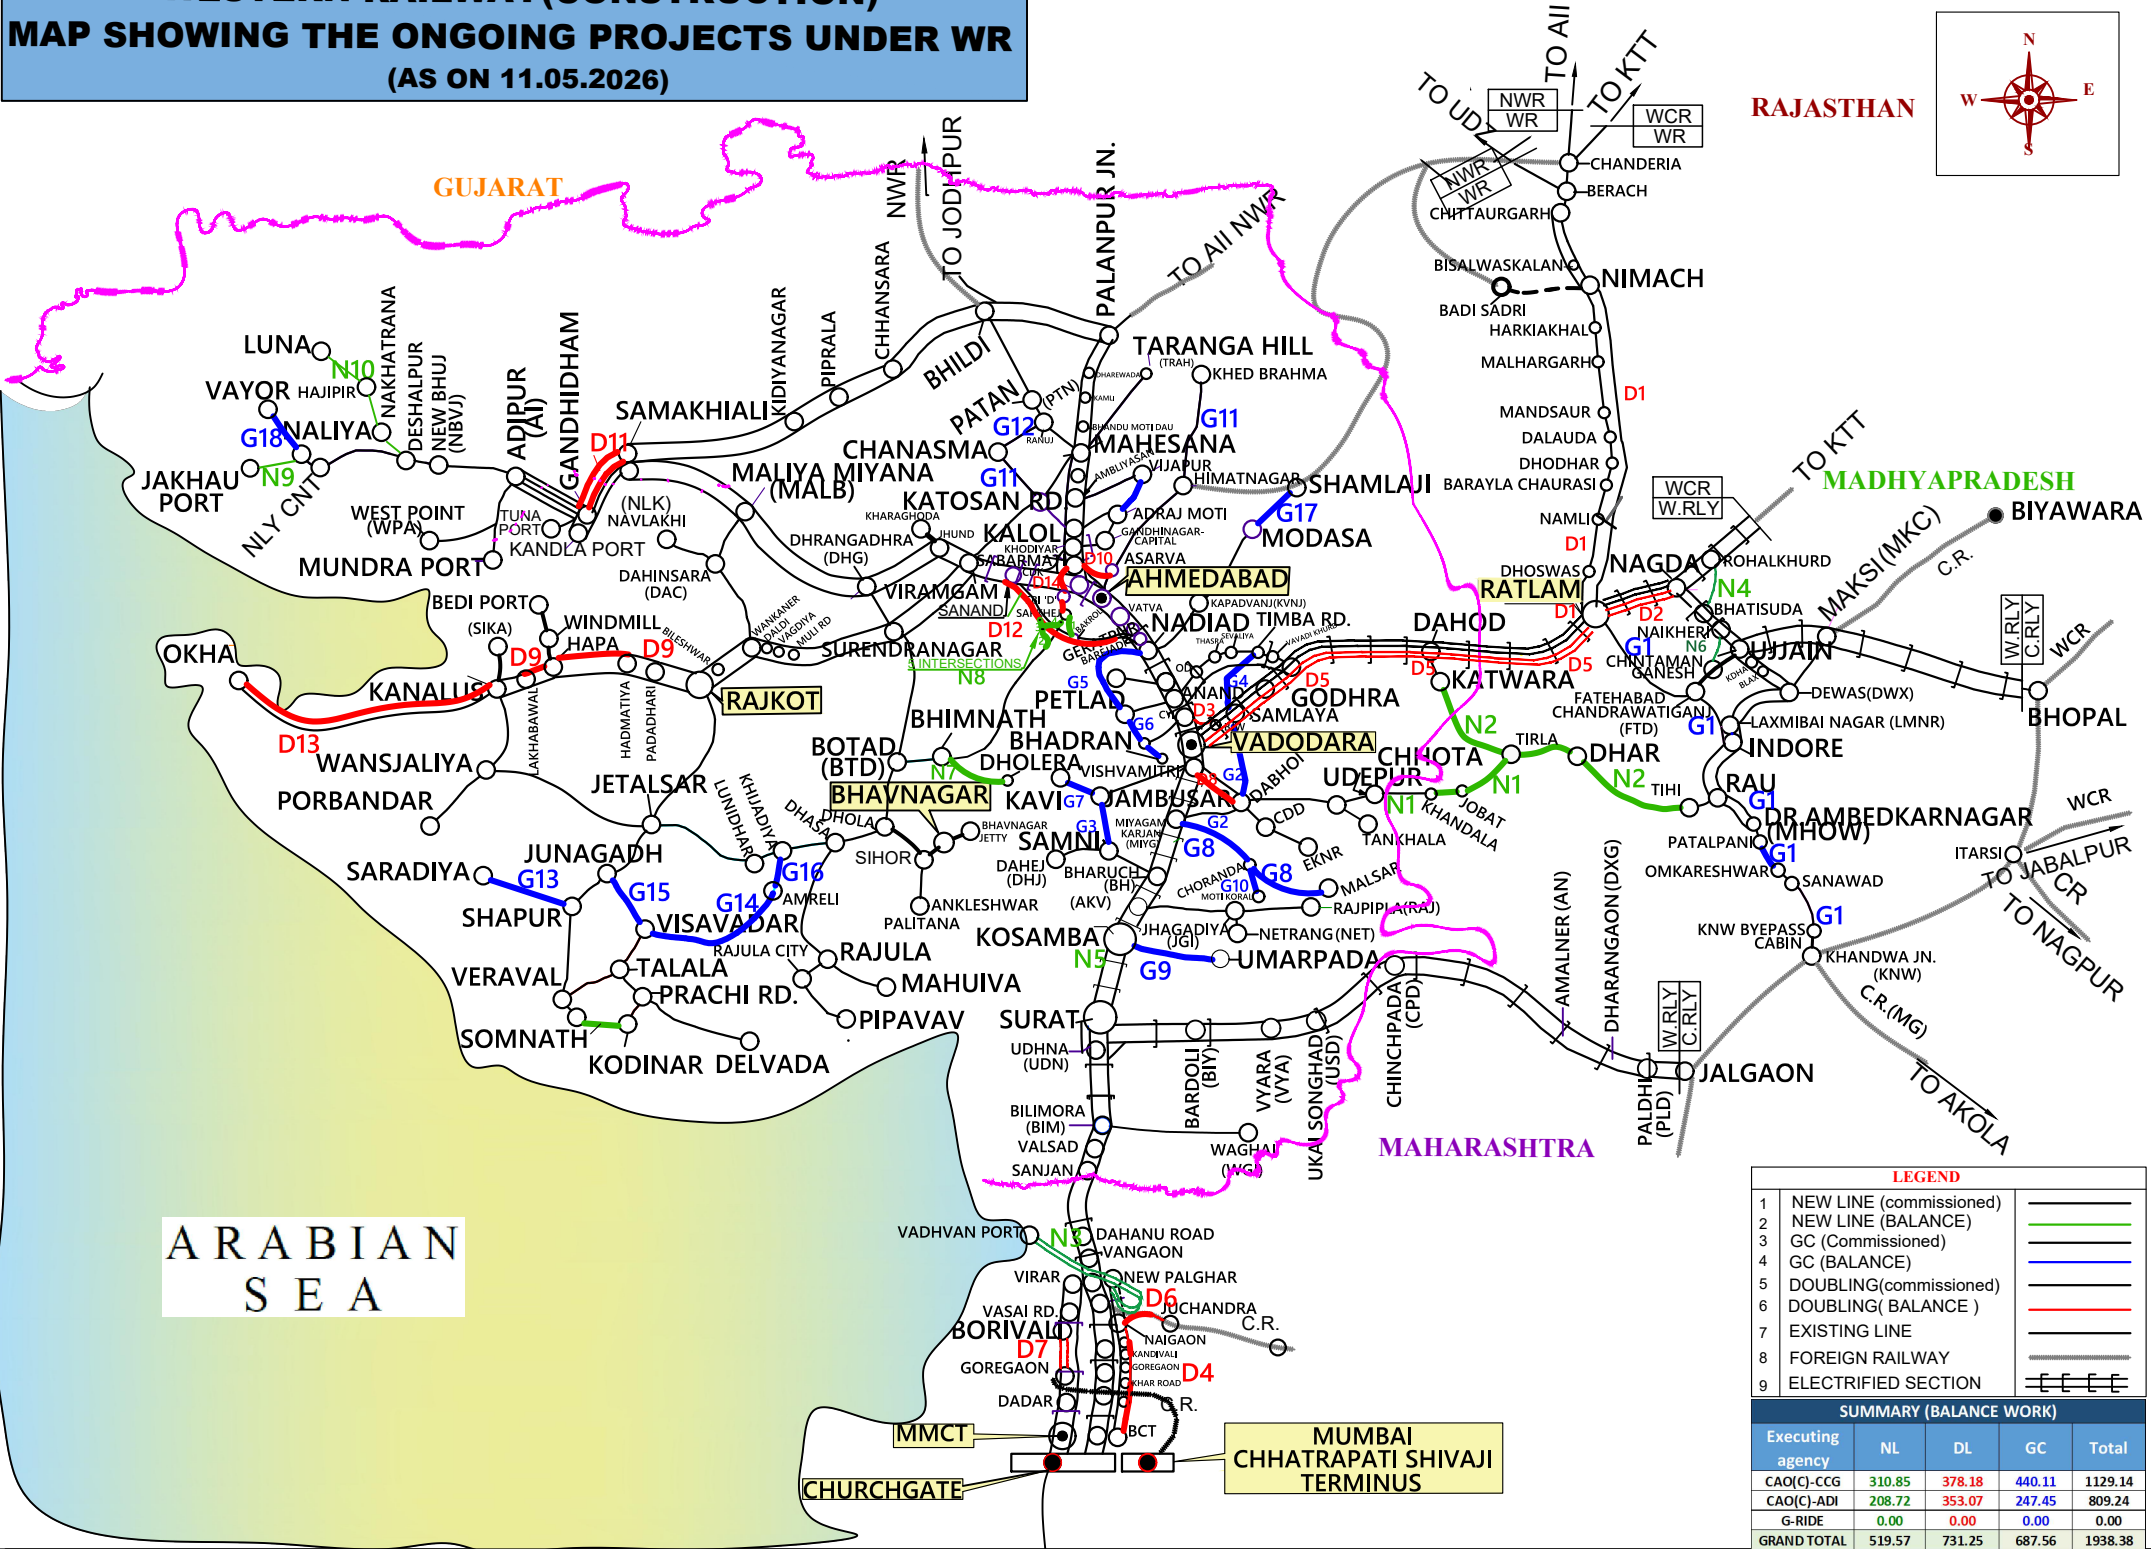

ONGOING PROJECTS						
SR. NO.	NAME OF PROJECTS	LENGTH (Km)	COMPLETED (Km)	BALANCE (Km)	AGENCY CE/IN CHARGE	TDC
CAO(C)-CCG						
NEW LINE						
N1	CHHOTA UDEPUR-DHAR	157.00	72.34	84.66	CPM-BRC	Feb-31
N2	DAHOD- INDORE	204.76	32.30	172.46	CE-C-III-CCG	May-28
N3	VADHVAN PORT-NEW PLAGHAR	22.23	0.00	22.23	CE-C-I-CCG	Dec-29
N4	NAGDA BYPASS	13.70	0.00	13.70	CE-C-III-CCG	Nov-28
N5	KOSAMBA ROR	9.20	0.00	9.20	CE-C-I-CCG	May-29
N6	UJJAIN BYPASS	8.60	0.00	8.60	CE-C-III-CCG	Not Fixed
TOTAL		415.49	104.64	310.85		
DOUBLING						
D1	NIMACH-RATLAM	133.00	133.00	0.00	CE-C-III-CCG	Comm.
D2	RATLAM-NAGDA 3RD AND 4TH LINE	41.38	0.00	41.38	CE-C-III-CCG	Mar-30
D3	MULTI. BET CHHAYAPURI-BAJVA	2.00	0.00	2.00	CPM-C-II-BRC	Jul-26
D4	6TH LINE BETWEEN BCT-BVI	29.53	13.41	16.12	CE-C-I-CCG	Mar-29
D5	VADODARA-RATLAM 3RD & 4TH LINE	273.12	0.00	273.12	CE-C-III-CCG	Mar-31
D6	VASAI BYEPASS NAIGAON-JUCHANDRA	5.73	0.00	5.73	CE-C-I-CCG	Mar-29
D7	EXT. OF HARBOUR LINE GMN-BVI	7.08	0.00	7.08	CE-C-I-CCG	Mar-29
D8	VISHVAMITRI-DABHOI	32.75	0.00	32.75	CPM-C-BRC	Dec-28
TOTAL		524.59	146.41	378.18		
GAUGE CONVERSION						
G1	RATLAM-MHOW-KHANDWA	303.95	218.43	85.52	CE-C-IV-CCG	Dec-30
G2	MIYAGAM-SAMLAYA	96.46	32.30	64.16	CPM-C-BRC	Jun-28
G3	SAMNI- JAMBUSAR	24.08	0.00	24.08	CPM-C-BRC	Jan-27
G4	SAMLAYA-TIMBA ROAD	53.53	0.00	53.53	CPM-C-BRC	Dec-27
G5	NADIAD-PETLAD	37.26	0.00	37.26	CPM-C-BRC	Jun-27
G6	PETLAD-BHADRAN	22.50	0.00	22.50	CPM-C-BRC	Feb-27
G7	JAMBUSAR-KAVI	26.36	0.00	26.36	CPM-C-BRC	Dec-28
G8	MIYAGAM KARAJAN- CHORANDA-MALSAR	38.00	0.00	38.00	CPM-C-BRC	Jul-27
G9	KOSAMBA-UMARPADA	69.70	0.00	69.70	CE-C-I-CCG	May-29
G10	CHORANDA-MOTI KORAL	19.00	0.00	19.00	CPM-C-BRC	Jun-27
TOTAL		690.84	250.73	440.11		
CAO(C)-ADI						
NEW LINE						
N7	BHIMNATH-DHOLERA	23.33	0	23.33	CPM-C-I-ADI	Jun-27
N8	INTERSECTIONS(5) BET. GERATPUR-SANAND AND BOTAD-ADI	16.51	1	15.51	CPM-I ADI	Jul-28
N9	NALIYA-JAKHAU PORT	24.88	0	24.88	CPM-II-ADI	Jun-27
N10	DESHALPAR-HAJIPUR-LUNA-VAYOR-LAKHPAT	145	0	145	CPM-C-II-ADI	Oct-26
TOTAL		209.72	1.00	208.72		
DOUBLING						
D9	RAJKOT-KANALUS	111.20	65.23	45.97	CPM-II-ADI	Dec-26
D10	Y CONNECTIVITY SABARMATI-ASARVA	0.90	0.00	0.90	CPM-I-ADI	Apr-26
D11	SAMAKHIALI – GANDHIDHAM QUAD	106.00	0.00	106.00	CPM-II-ADI	Sep-27
D12	4 TH LINE GERATPUR-SANAND	38.20	0.00	38.20	CPM-I-ADI	Jul-28
D13	DEVBHUMI DWARKA DL OKHA-	141.00	0.00	141.00	CPM-C-I-ADI	Dec-29
D14	SABARMATI-SARKHEJ	21.00	0.00	21.00	CPM-C-I-ADI	May-28
TOTAL		418.30	65.23	353.07		
GAUGE CONVERSION						
G11	KATOSAN ROAD- CHANASMA	51.72	51.72	0.00	G RIDE	Completed commi. yet to be done
G12	CHANASMA-RANUJ	12.84	12.84	0.00	G RIDE	Completed commi. yet to be done
G13	SHAPUR-SARADIYA GC (MM of RJT-VRL)	46.00	0.00	46.00	CPM-C-II-ADI	Not Fixed
G14	KHUADIYA- VISAVADAR	91.27	0.00	91.27	CPM-I-ADI	May-26
G15	JUNAGADH- VISAVADAR-RVNL	42.28	0.00	42.28	CPM-II-ADI	Not Fixed
G16	KHUADIYA- AMRELI	16.60	0.00	16.60	CPM-II-ADI	May-26
G17	ADI-HMT INCL. MODASA SHAMLAJI NL	114.84	88.19	26.65	CPM-II-ADI	Not Fixed
G18	BHUJ-NALIYA INCLU. NALIYA-VYOR NL	127.75	103.10	24.65	CPM-II-ADI	Feb-27
TOTAL		503.30	255.85	247.45		

SUMMARY (BALANCE WORK)				
Executing agency	NL	DL	GC	Total
CAO(C)-CCG	310.85	378.18	440.11	1129.14
CAO(C)-ADI	208.72	353.07	247.45	809.24
G-RIDE	0.00	0.00	0.00	0.00
GRAND TOTAL	519.57	731.25	687.56	1938.38
